



PROPOSAL RESPONSE FOR
USTA League Scheduler Platform

Submitted by: AMEO Analytics

1533 Catron Ave. SE
Albuquerque, NM 87123
Phone: (505) 241-9096
Email: ameo.analytics@gmail.com

August 22, 2025

Contents

1	General Information	4
2	Company Profile	4
3	Project Information	5
3.1	Technologies, Systems Resources, and Assets	5
3.1.1	Current Implementation Technology Stack	5
3.1.2	Proposed Production Infrastructure	6
3.2	Personnel Management and Hiring Strategy	6
3.2.1	Core Team Structure	6
3.3	Payment Requirements and Financial Structure	6
3.4	Environmental Responsibility and Sustainability Commitment	6
3.4.1	Green Technology Practices	6
3.4.2	Renewable and Recyclable Products	7
4	Financial Proposal	7
4.1	Project Overview	7
4.2	Detailed Project Cost Breakdown	7
4.3	Payment Schedule and Milestones	7
4.4	Cost Justification and Value Proposition	8
4.5	Ongoing Support and Maintenance Options	8
4.5.1	Additional Services (Hourly Rates)	8
4.6	Financial Terms and Conditions	8
4.7	Investment Protection and Guarantees	8
5	Approach & Strategy	9
5.1	Project Management Methodology	9
5.2	Coordination with USTA	9
5.3	Third-Party Vendors	9
5.4	Required USTA Resources	9
5.5	Key Skills Needed from USTA Team	9
6	Schedule	9
6.1	Phase 1: Discovery & Software Architecture Design (Weeks 1-6)	10
6.2	Phase 2: Core Development (Weeks 7-12)	10
6.3	Phase 3: Beta Testing & Product Hardening (Weeks 13-16)	10
6.4	Phase 4: Deployment & Go-Live (Weeks 17-19)	11
6.5	Key USTA Deliverables	11
6.6	Current Project Considerations	11
7	Feature Set and Functional Capabilities	12
7.1	Core Application Infrastructure	12
7.1.1	Administrative Dashboard and System Navigation	12
7.1.2	Facility Resource Management	13
7.1.3	League Administration and Governance	14
7.1.4	Team Management and Coordination	15
7.2	Advanced Match Scheduling and Optimization Framework	16

7.2.1	Automated Match Generation and Distribution	16
7.2.2	Intelligent Automated Scheduling Engine	16
7.2.3	Interactive Manual Scheduling Interface	17
7.3	Data Integration and Management Framework	19
7.3.1	Advanced Import/Export Architecture	19
7.3.2	Administrative Command Line Interface	19
7.4	Supplementary Capabilities and Enhancement Features	19
7.5	Technical Architecture and Implementation Framework	20
8	Disclosures	21
8.1	I. Operational/Service Compliance (Last 5 Years)	21
8.2	II. Criminal Convictions (Last 5 Years)	21
9	Claims/Litigation	21
10	Finances	21
11	Company Overview	21
11.1	Business Classification	21
12	Conflicts of Interest	22
13	Contract Terms	22
13.1	Proposed Service Agreement Framework	22
13.1.1	Information Security Program and Data Privacy	22
13.1.2	Standard Terms	22
14	Other Information	22



AMEO Analytics
Ron and Susan Oldfield
1533 Catron Ave. SE
Albuquerque, NM 87123
Phone: (505) 241-9096
Email: ameo.analytics@gmail.com

August 18, 2025

Anna DiStefano
Buyer, Purchasing
United States Tennis Association Incorporated
2500 Westchester Avenue, Suite 411
Purchase, NY 10577

Re: USTA League Scheduler Platform Proposal

Dear Ms. DiStefano,

AMEO Analytics is pleased to submit this proposal for the USTA League Scheduler Platform. We are a newly formed LLC established specifically to partner with the United States Tennis Association on this transformative project.

In anticipation of this CFP, we have developed a sophisticated tennis scheduling prototype that addresses many of the core capabilities outlined in the RFP's services overview. Our prototype has been demonstrated, evaluated, and improved by Ben Friendly and Kelly Ferris, USTA league coordinators for Northern New Mexico and Phoenix. While our initial prototype contains substantial functionality, full production deployment requires additional work that includes testing, security hardening, feature enhancement, cloud infrastructure deployment, and Tennislink integration.

This proposal includes detailed technical descriptions, implementation timeline, comprehensive existing and planned features, and competitive pricing. We have thoroughly reviewed all RFP requirements and are confident our solution exceeds expectations while delivering exceptional value.

Thank you for considering AMEO Analytics for this important initiative. If selected to move forward, we look forward to presenting our proposal and providing a demonstration of our current prototype. As USTA members and avid tennis players, we're excited at the prospect of helping USTA transform league scheduling nationwide.

Sincerely,

Ron and Susan Oldfield

Attachments: Complete Proposal Response with Technical Specifications, Implementation Plan, and Financial Details

7 Feature Set and Functional Capabilities

This section presents a comprehensive description of the system’s feature set, organized by functional domain and implementation complexity. Our current prototype² already contains draft versions of the features identified in Section I of the RFP. Table 2 provides a comprehensive mapping of the required features specified in the RFP Services Overview to the current prototype implementation status and relevant documentation sections.

Table 2: Implementation Status of Required RFP Features: Current Prototype Capabilities and Planned Development Timeline

Required Feature	Current Status
Venue and Court Availability Management	In Prototype
UI for facilities/admins to enter availability	In Prototype
Ability to ingest team matchups from Tennislink	Phase 1 and 2
Blackout dates	In Prototype
Match Generation with Home/away balance	In Prototype
Scheduling with Split start times	In Prototype
Facility management	In Prototype
Scheduling Conflict Avoidance	In Prototype
Match deletion/editing	In Prototype
Write schedule back to Tennislink	Phase 1 and 2

7.1 Core Application Infrastructure

7.1.1 Administrative Dashboard and System Navigation

The system provides a centralized administrative interface designed to facilitate efficient operation management and system oversight:

- **Unified Navigation Architecture:** Implements intuitive access pathways to all major functional modules (Facilities, Leagues, Teams, Matches) through a hierarchical menu system
- **Import/Export:** Comprehensive YAML and JSON data interchange functionality with structured schema validation and bulk operations support for leagues, facilities, teams, and match data
- **System Health Monitoring:** Continuous monitoring of database connectivity, system performance indicators, and operational health metrics
- **Administrative Workflows:** Streamlined access to frequently executed operations including automated match generation and intelligent scheduling procedures
- **Responsive User Interface:** Modern Bootstrap-based interface architecture ensuring cross-platform compatibility and quality user experience

²The current prototype version of the AMEO Analytics scheduling software was developed to demonstrate capability only. A full production version requires a rigorous software-quality assessment and thorough testing and integration of several additional capabilities to ensure security and compatibility with Tennislink software.

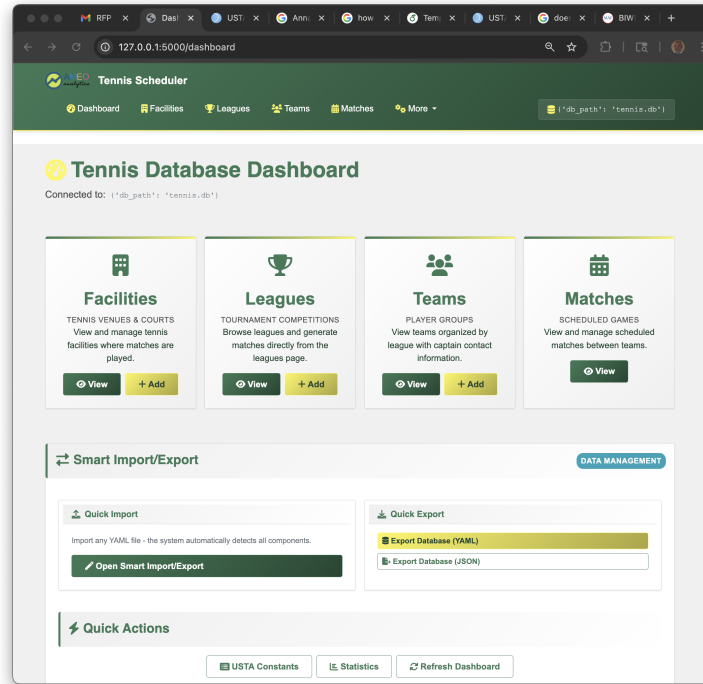


Figure 1: Administrative Dashboard Interface

7.1.2 Facility Resource Management

The system implements comprehensive facility management capabilities designed to optimize resource allocation and operational efficiency:

- **Facility Information Repository:** Maintains detailed facility profiles including nomenclature, geographical coordinates, court inventory, and operational schedules
- **Advanced Scheduling Infrastructure:** Supports complex temporal availability patterns including weekly recurring schedules, exceptional blackout periods, and court-specific operational constraints
- **Resource Capacity Optimization:** Implements real-time tracking of court availability and temporal slot allocation for enhanced scheduling efficiency
- **Performance Analytics:** Provides comprehensive facility utilization metrics including court occupancy rates, usage distribution analysis, and operational efficiency indicators
- **Administrative Interface:** Features advanced form-based management tools for configuring weekly operational schedules and temporal availability restrictions
- **Data Organization Tools:** Implements multi-criteria sorting capabilities based on facility attributes including nomenclature, location, court capacity, and availability status

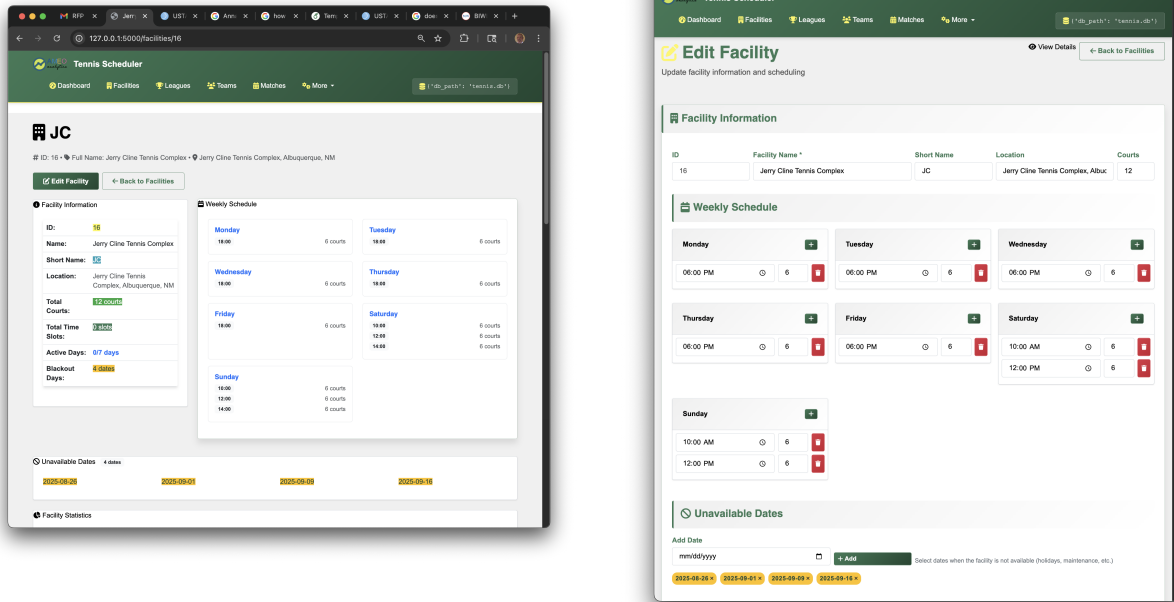


Figure 2: Facility Management Interface: (left) venue details and court information display, (right) facility editing and availability scheduling configuration

7.1.3 League Administration and Governance

The application provides comprehensive support for league management aligned with USTA organizational standards:

- **USTA Compliance Framework:** Full implementation of official USTA league classification system including year, section, region, age group, and division taxonomies
- **Organizational Scheduling Parameters:** Configurable league-wide scheduling preferences including primary playing days, alternative scheduling periods, and seasonal operational constraints
- **Competition Structure Configuration:** Comprehensive match configuration capabilities including line specifications, tournament format definitions, and temporal round organization
- **Seasonal Operations Management:** Administrative tools for defining season parameters including start/end dates, round scheduling methodology, and league-specific operational rules
- **Team Organizational Framework:** Hierarchical team management within league structures including relationship mapping and scheduling interdependencies

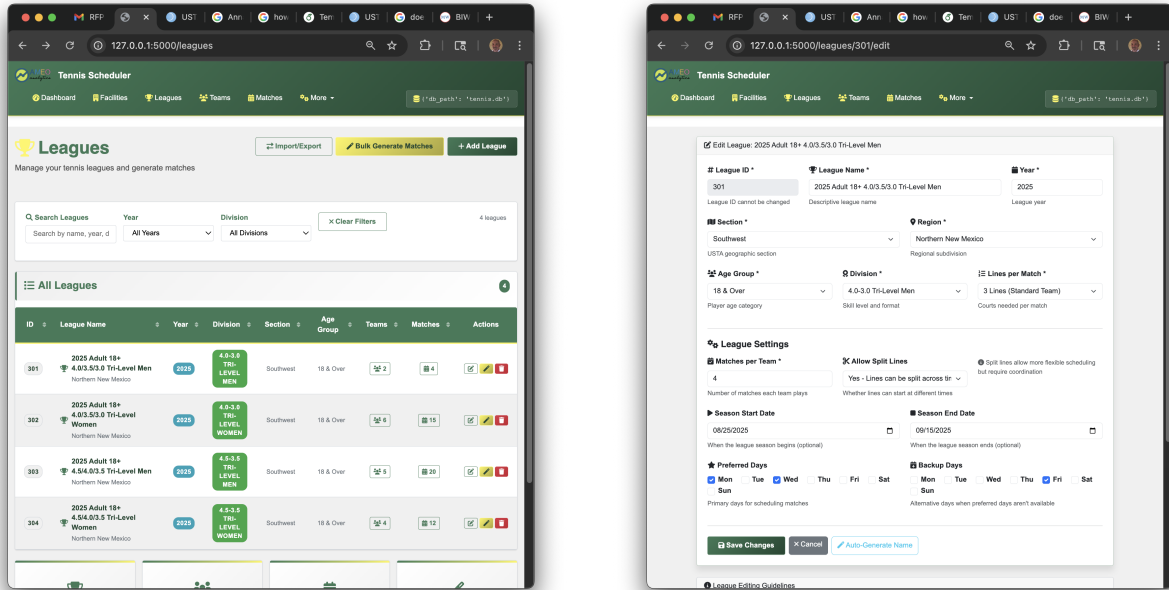


Figure 3: League Administration Interface: (left) USTA league listing with organizational structure, (right) league configuration with scheduling parameters and competition structure

7.1.4 Team Management and Coordination

The system provides sophisticated team management capabilities with enhanced facility coordination:

- **Multi-Facility Assignment Architecture:** Implementation of hierarchical facility preference systems enabling teams to maintain multiple venue associations with priority-based ordering:
 - Primary facility designation for initial scheduling optimization
 - Secondary facility allocations providing scheduling flexibility and conflict resolution
 - Dynamic priority reordering through intuitive drag-and-drop interface mechanisms
 - Comprehensive facility management through web-based administrative interfaces
- **Team-Specific Scheduling Preferences:** Configurable temporal preferences including preferred playing days and availability constraint management
- **League Integration Protocols:** Advanced filtering and organizational tools providing detailed league-specific team information and hierarchical relationships
- **Intelligent Facility Selection:** Automated facility selection algorithms considering real-time availability, capacity constraints, and team preference hierarchies

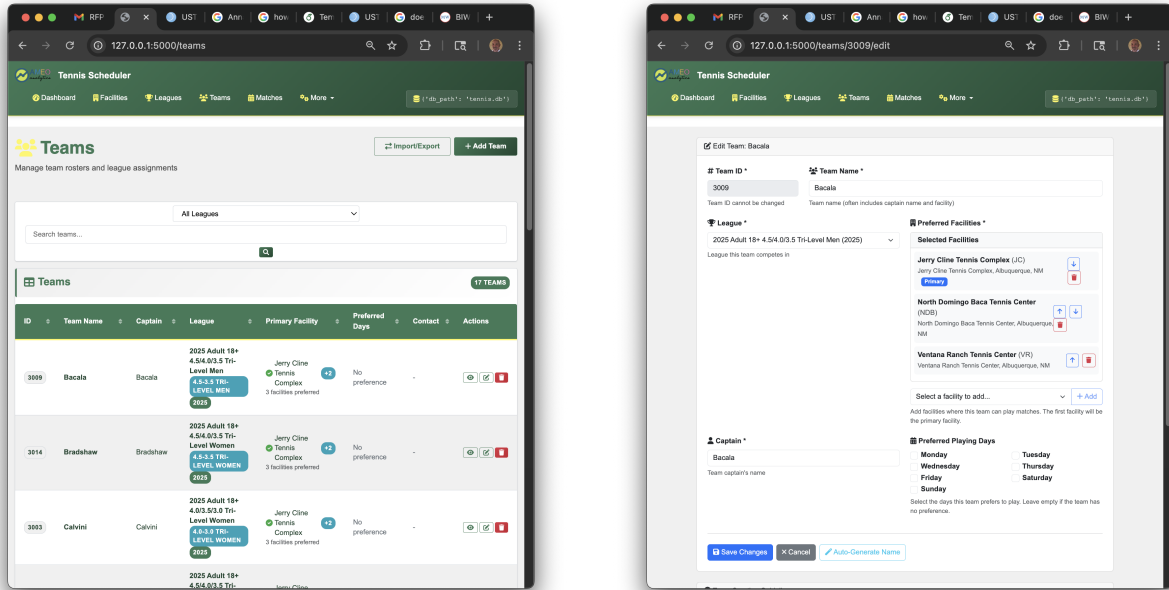


Figure 4: Team Management Interface: (left) team listing with league filtering and facility assignments, (right) team editing with multi-facility preference configuration

7.2 Advanced Match Scheduling and Optimization Framework

7.2.1 Automated Match Generation and Distribution

The system implements sophisticated algorithms for fair and balanced match generation across league structures:

- **Round-Robin Tournament Generation:** Implements complete round-robin algorithms ensuring every team competes against every other team exactly once per round, with balanced match distribution and equitable home/away venue assignments
- **Venue Equity Optimization:** Employs mathematical optimization algorithms to equalize home and away match distributions across all participating teams
- **Load Balancing Algorithms:** Minimizes variance in total match assignments per team to ensure competitive balance across the league structure
- **Configurable Tournament Structure:** Provides flexible round configuration capabilities including customizable match quantities and line specifications based on league requirements
- **Constraint Validation Framework:** Implements comprehensive validation systems preventing impossible scheduling scenarios through team availability analysis

7.2.2 Intelligent Automated Scheduling Engine

The application features a sophisticated multi-algorithm scheduling engine designed to optimize match placement:

- **Team Preference Analysis:** Implements intelligent analysis algorithms for both team's preferred playing schedules and availability constraints
- **League Priority Hierarchies:** Considers organizational scheduling preferences including primary playing days, alternative playing days, and priorities for in-round scheduling
- **Real-Time Availability Processing:** Features dynamic court availability verification with integrated blackout period handling and capacity management
- **Conflict Resolution Protocols:** Implements comprehensive conflict detection preventing team double-booking and facility resource overbooking across all scheduling operations
- **Quality Assessment Metrics:** Features quantitative scoring system (0-100 scale) evaluating in-round scheduling, team, league, and facility preference alignment to assign a score to a single scheduled match
- **Scheduled Quality Index:** Assigns an aggregate quality score, defined as a *Schedule Quality Index (SQI)* to a set of matches
- **Iterative Optimization Algorithms:** Employs multi-iteration scheduling with randomized seed generation to identify a schedule with the highest SQI
- **Adaptive Line Distribution:** Intelligent line distribution algorithms to accommodate facility capacity limitations (e.g., all lines together or split across consecutive time slots)

7.2.3 Interactive Manual Scheduling Interface

The system provides comprehensive manual scheduling capabilities for administrative oversight and customization:

- **Visual Temporal Navigation:** Implements intuitive date browsing interface displaying quality assessment scores and comprehensive facility information
- **Dynamic Conflict Visualization:** Real-time display of existing match conflicts, court availability status, and potential scheduling conflicts
- **Multi-Modal Scheduling Options:** Flexible scheduling methodologies including:
 - All lines together: All match lines scheduled simultaneously
 - Split lines: Match lines split across multiple time slots
 - Custom scheduling: Individual line scheduling providing maximum administrative flexibility (TODO)
- **Transaction Preview Capabilities:** Comprehensive preview functionality displaying all proposed database modifications prior to commitment
- **Validation and Warning Systems:** Advanced warning mechanisms identifying scheduling conflicts and suboptimal administrative choices

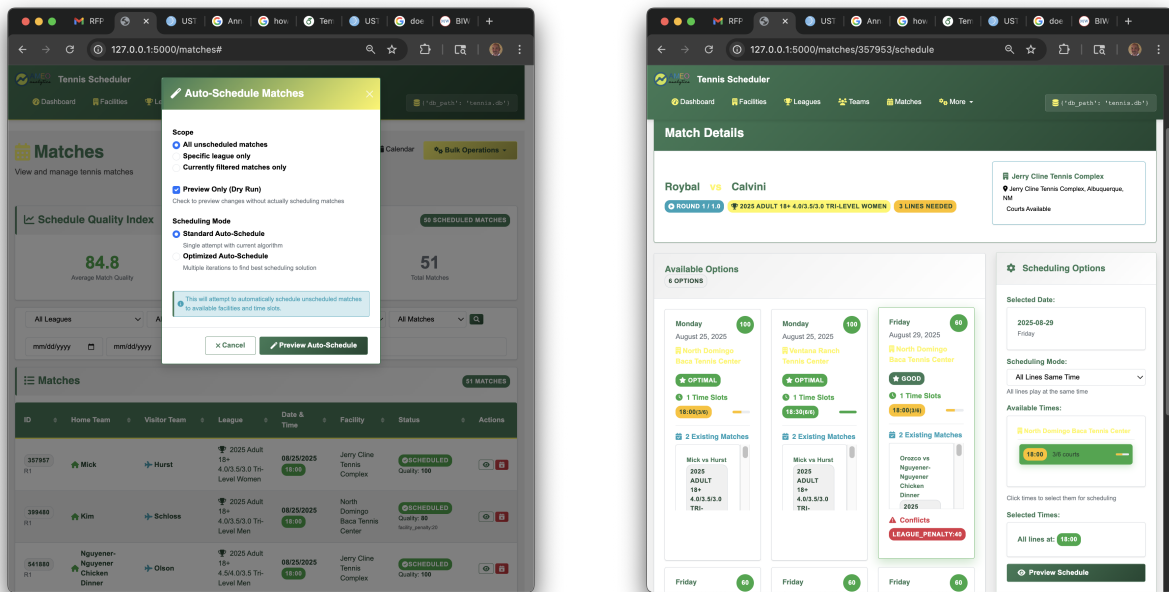


Figure 5: Scheduling Interfaces: (left) match listing with scheduling controls and quality assessment highlighting the bulk match-scheduling capability, (right) individual match scheduling showing options and with quality scores.




Figure 6: Mobile-phone interface for scheduled matches.
